BRAHMAPUTRA CRACKER AND POLYMER PROJECT

SL NO	DESCRIPTION	
A	**GENERAL**	
01	PROJECT ZERO DATE	
02	APPOINTMENT OF EPCM CONSULTANT	
B	**INFRASTRUCTURE/ENABLING WORKS**	
01	LAND ACQUISITION	ACT
02	OVERALL PLOT PLAN	ACT
03	AWARD OF GEO-TECH./TOPOGRAPHICAL TENDERS	ACT
04	SITE DEVELOPMENT	ACT/ SCH
C	**PROCESS PACKAGES**	
01	SELECTION OF PROCESS LICENSORS	ACT
02	PROCESS PACKAGE FOR ETHYLENE CRACKER UNIT	ACT
03	PROCESS PACKAGES FOR DOWN STREAM UNITS LLDPE/HDPE SWING UNIT	ACT
	PP UNIT	ACT
04	PROCESS PACKAGE FOR C2/C3 SEPARATION & PIPELINES	ACT
05	PROCESS PACKAGE FOR UTILITIES & OFFSITES	ACT
D	**ENGINEERING**	
01	GAS SWEETENING & C2 / C3 SEPARATION UNITS	ACT/ SCH
02	ETHYLENE CRACKER UNIT	ACT/ SCH
03	DOWN STREAM UNITS - LLDPE / HDPE SWING UNIT	ACT/ SCH
04	DOWN STREAM UNITS - PP UNIT	ACT/ SCH
05	UTILITIES & OFFSITES	ACT/ SCH
06	PIPELINES & TERMINAL WORK	ACT/ SCH

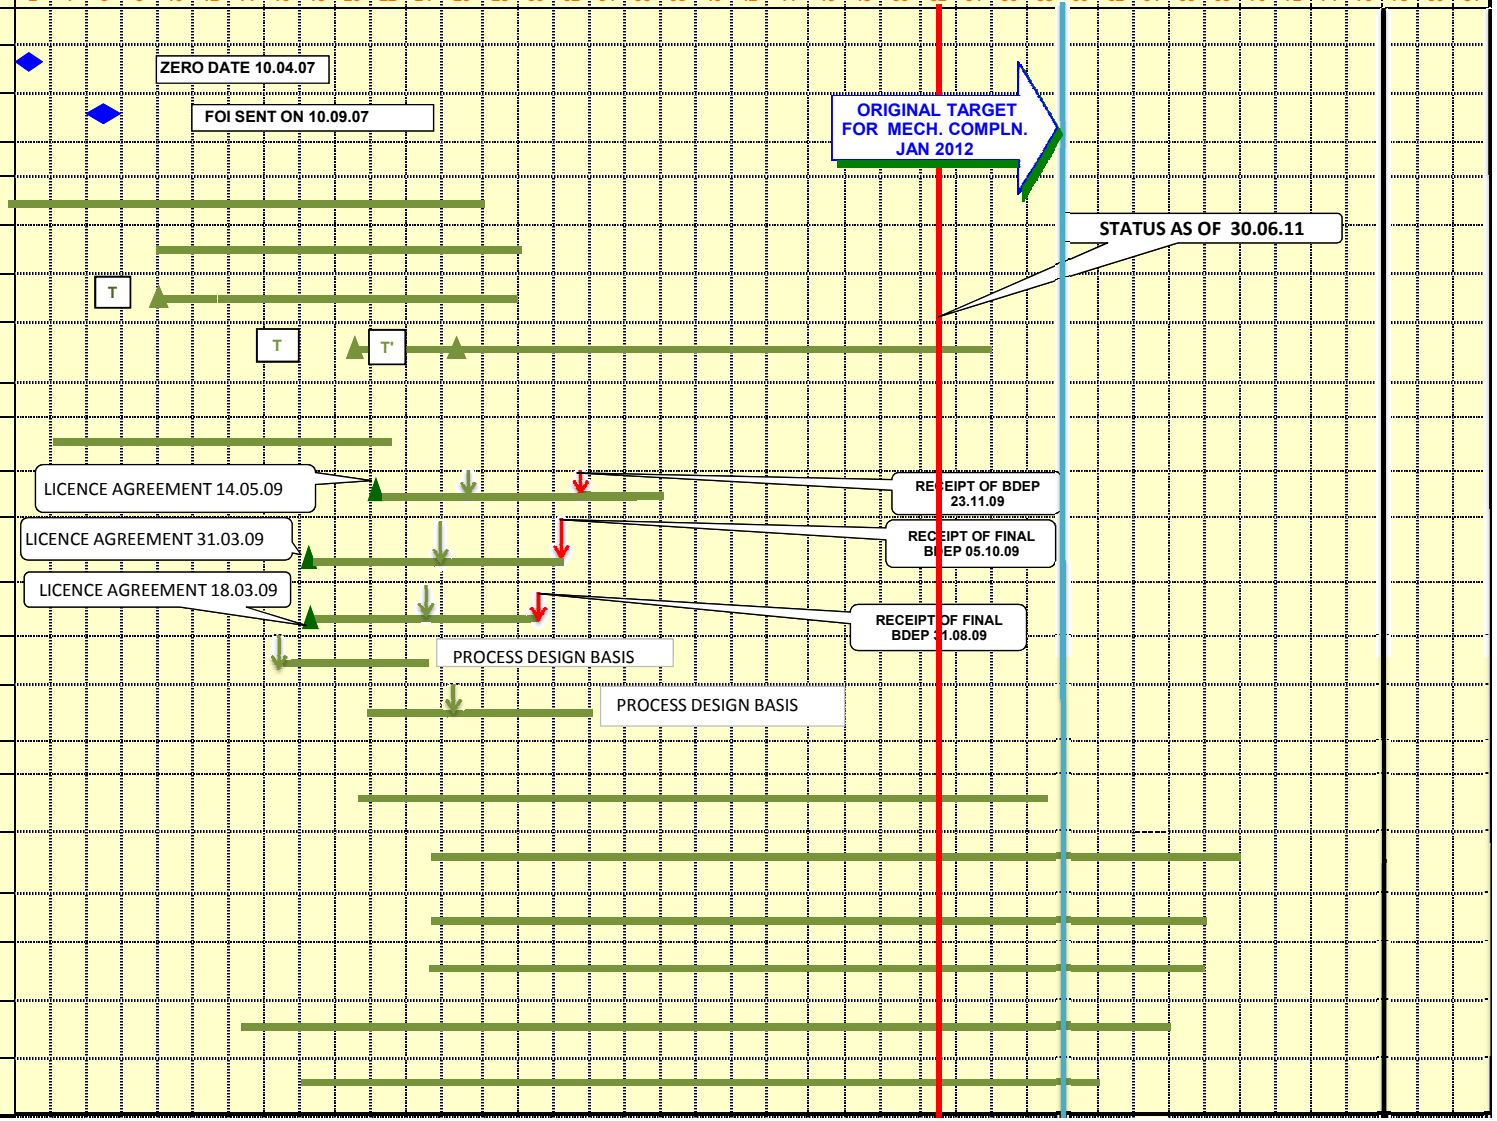

BRAHMAPUTRA CRACKER AND POLYMER PROJECT

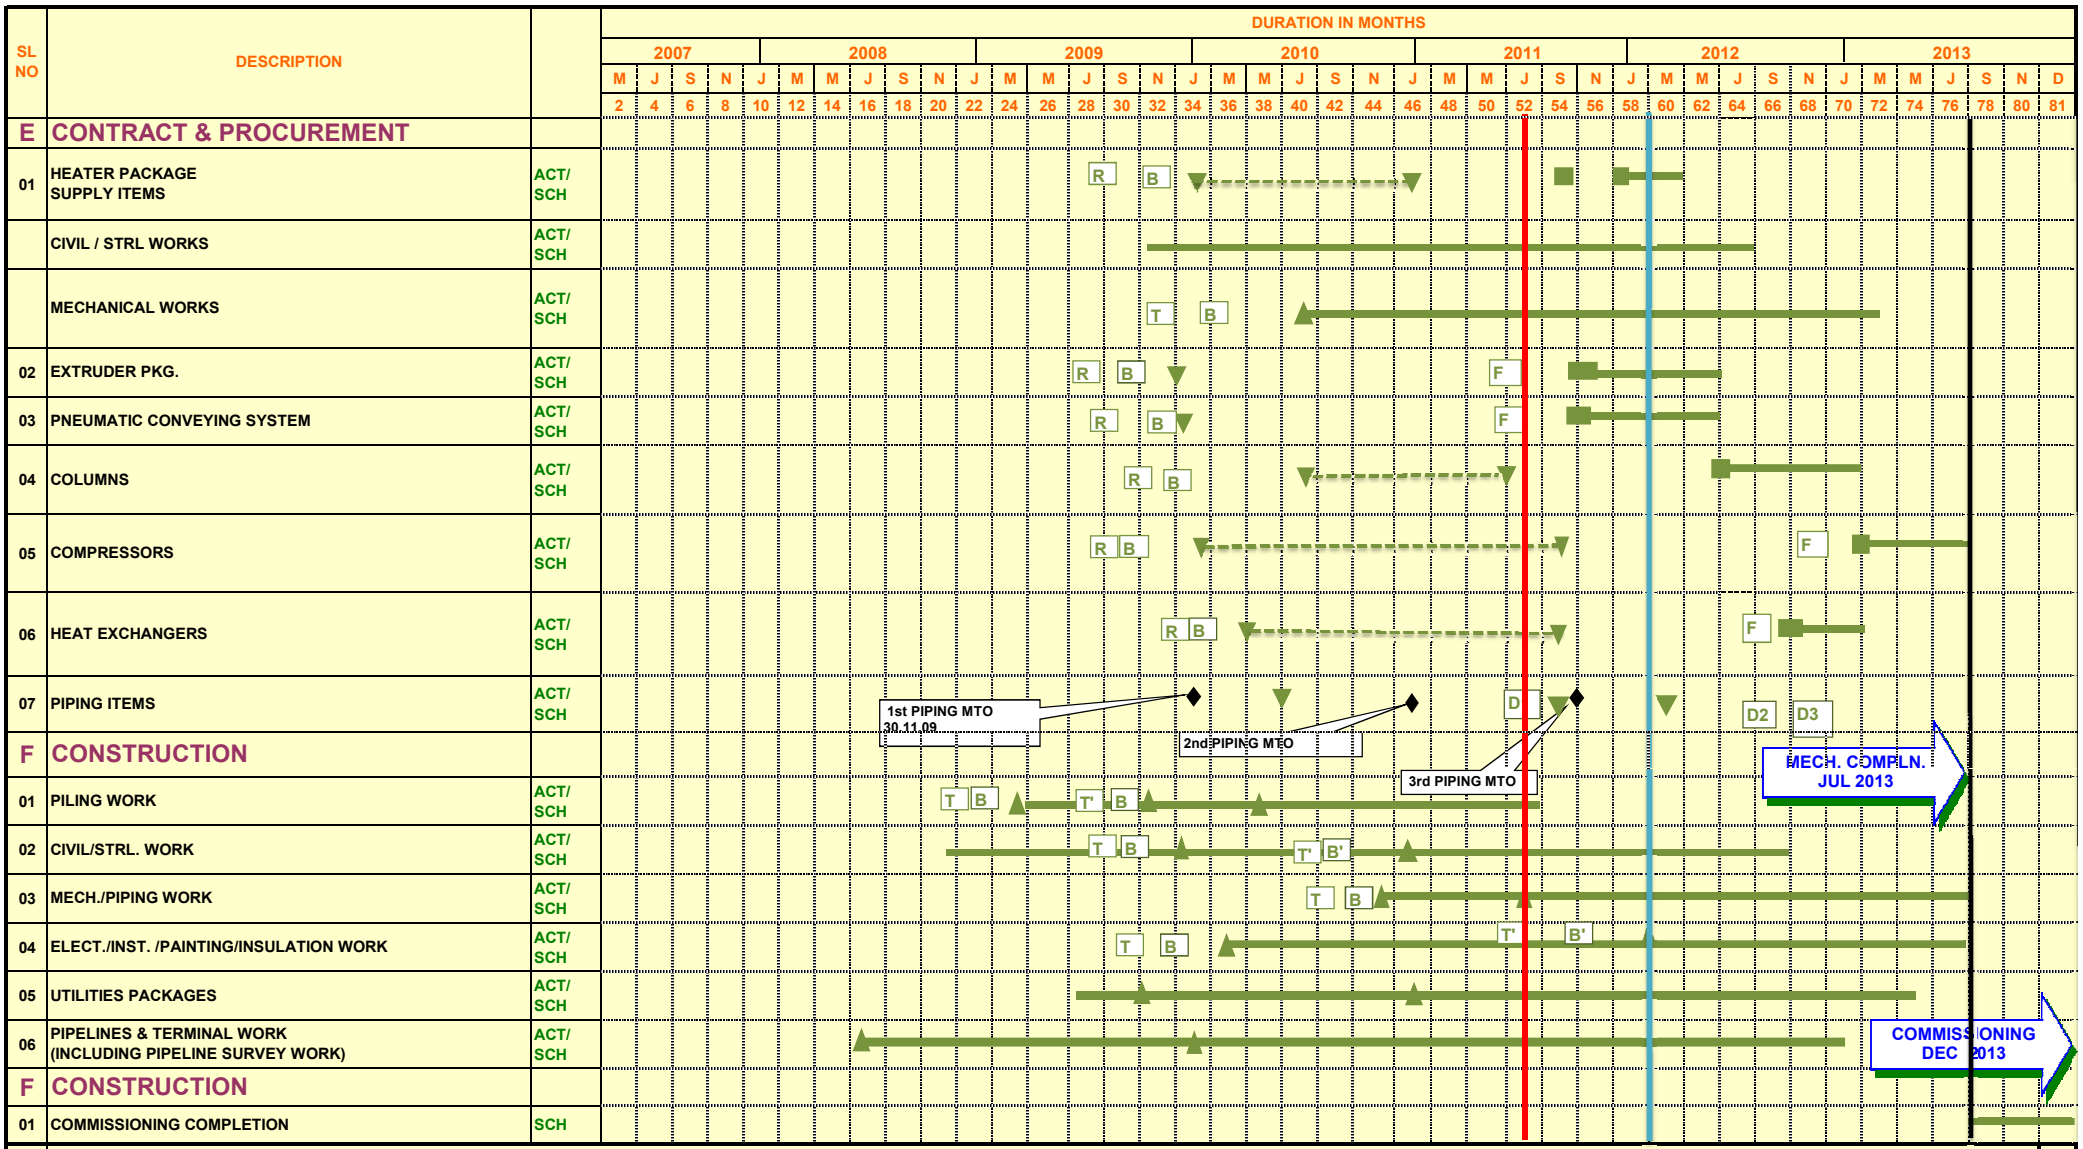

LEGEND : T ISSUE TENDER ▲ AWARD OF CONTRACT D EX. WORKS DELIVERY ■ MATERIAL DELIVERY AT SITE ACTIVITY COMPLETED / IN PROGRESS / TARGETED COMPLETION

R MATERIAL REQ. B RECEIVE BIDS F FOB DELIVERY ♦ MTO RELEASE ▼ PLACE ORDER

PLANT : **BRAHMAPUTRA PETROCHEMICAL COMPLEX**

LOCATION : **LEPETKATA, ASSAM**

OWNER : **M/S. BRAHMPUTRA CRACKER & POLYMER LIMITED**

OVERALL PROJECT SCHEDULE

NB : Time Lines shown prior to Jun'11 are as per actual status of their occurence & those shown beyond Jun'11 are as per revised mechanical completion schedule of Jul'13
